Studio exterior opening coordination

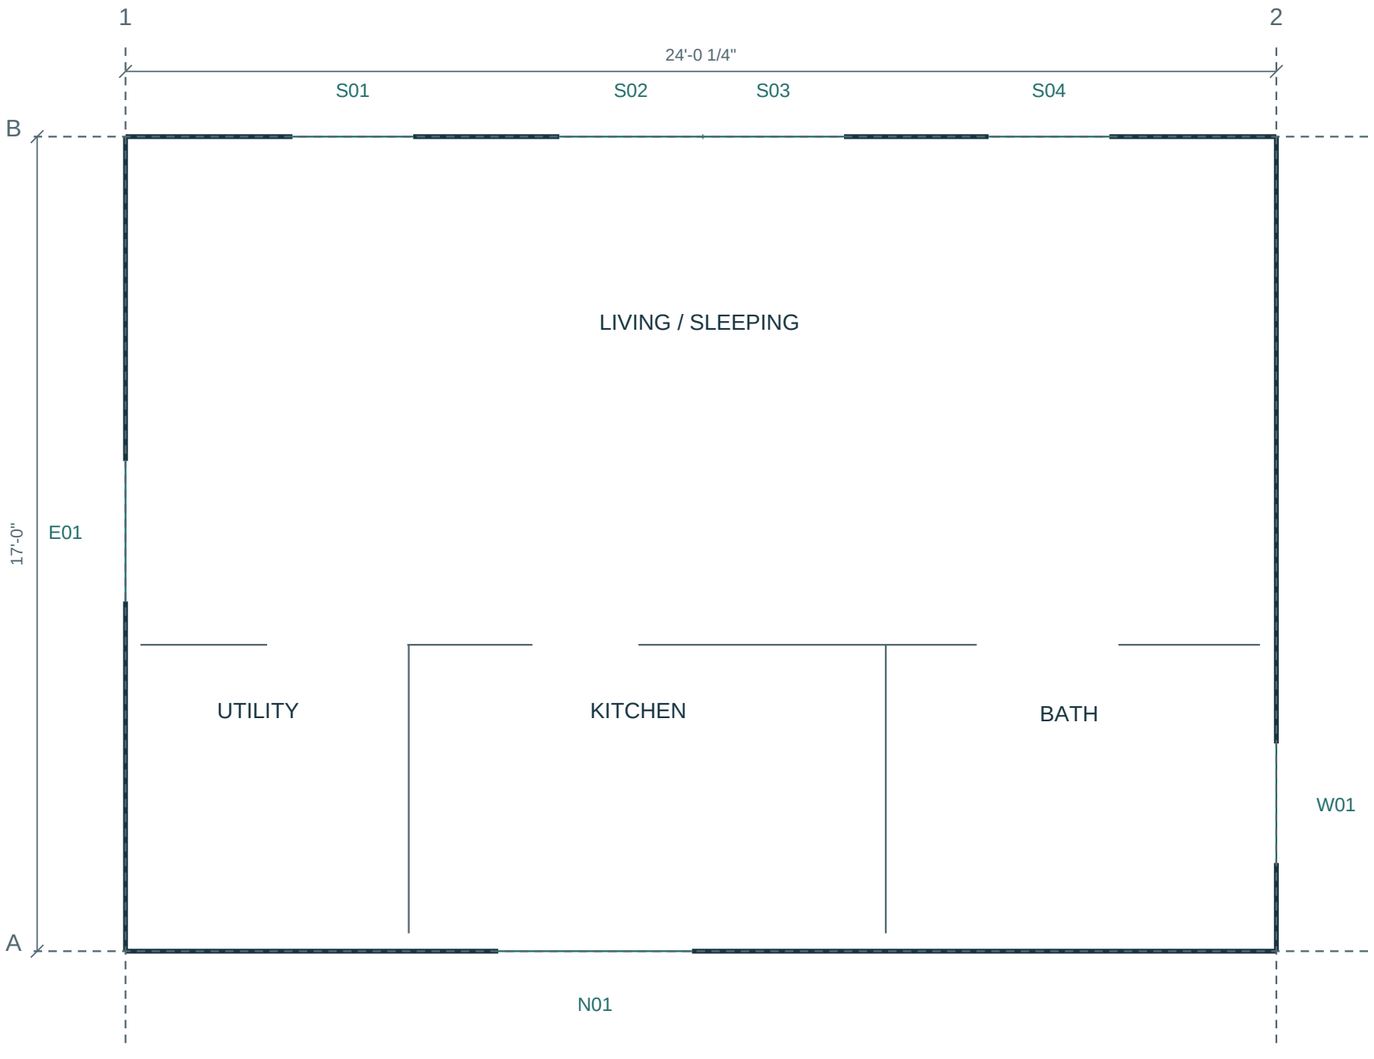

EXTERIOR OPENING SCHEDULE / INCHES

ID	TYPE	START*	END*	PIER*	SOURCE SIZE
T / SOUTH | WALL 288.25 | END PIER* 41.8					
S01	WINDOW	41.8	72.1	41.8	30 x 60
S02	VENT	108.7	144.5	36.6	36 x 80
S03	DOOR	144.5	180	0	36 x 80
S04	WINDOW	216.2	246.4	36.2	30 x 60
B / NORTH | WALL 288.25 | END PIER* 146.4					
N01	WINDOW	93.3	141.9	93.3	48 x 36
R / WEST | WALL 204 | END PIER* 22.1					
W01	WINDOW	152	181.9	152	12 x 36
L / EAST | WALL 204 | END PIER* 87.6					
E01	DOOR	81.2	116.4	81.2	36 x 80

* Approximate trace in inches. Pier is clear plan distance from prior traced edge or starting corner. Nominal sizes are source elevation labels. Confirm frame OD, RO, sill and head with selected assemblies.

Plan width 288.25 in; elevation 288 in. W01 is labeled 12 x 36 and drawn horizontally; confirm width and height. Entry door and vented glazing require a combined assembly RO.

Source interior tags: 32 and 33 in plus 36 in bath slider. Coordinate equipment and kitchen access.

DATUM AND STATION METHOD

T/B stations run plan left to right. L/R stations run plan top to bottom. 1-2 and A-B identify the exterior footprint datums. Opening stations are approximate trace measurements from an NTS reference.

Parkview exterior opening coordination

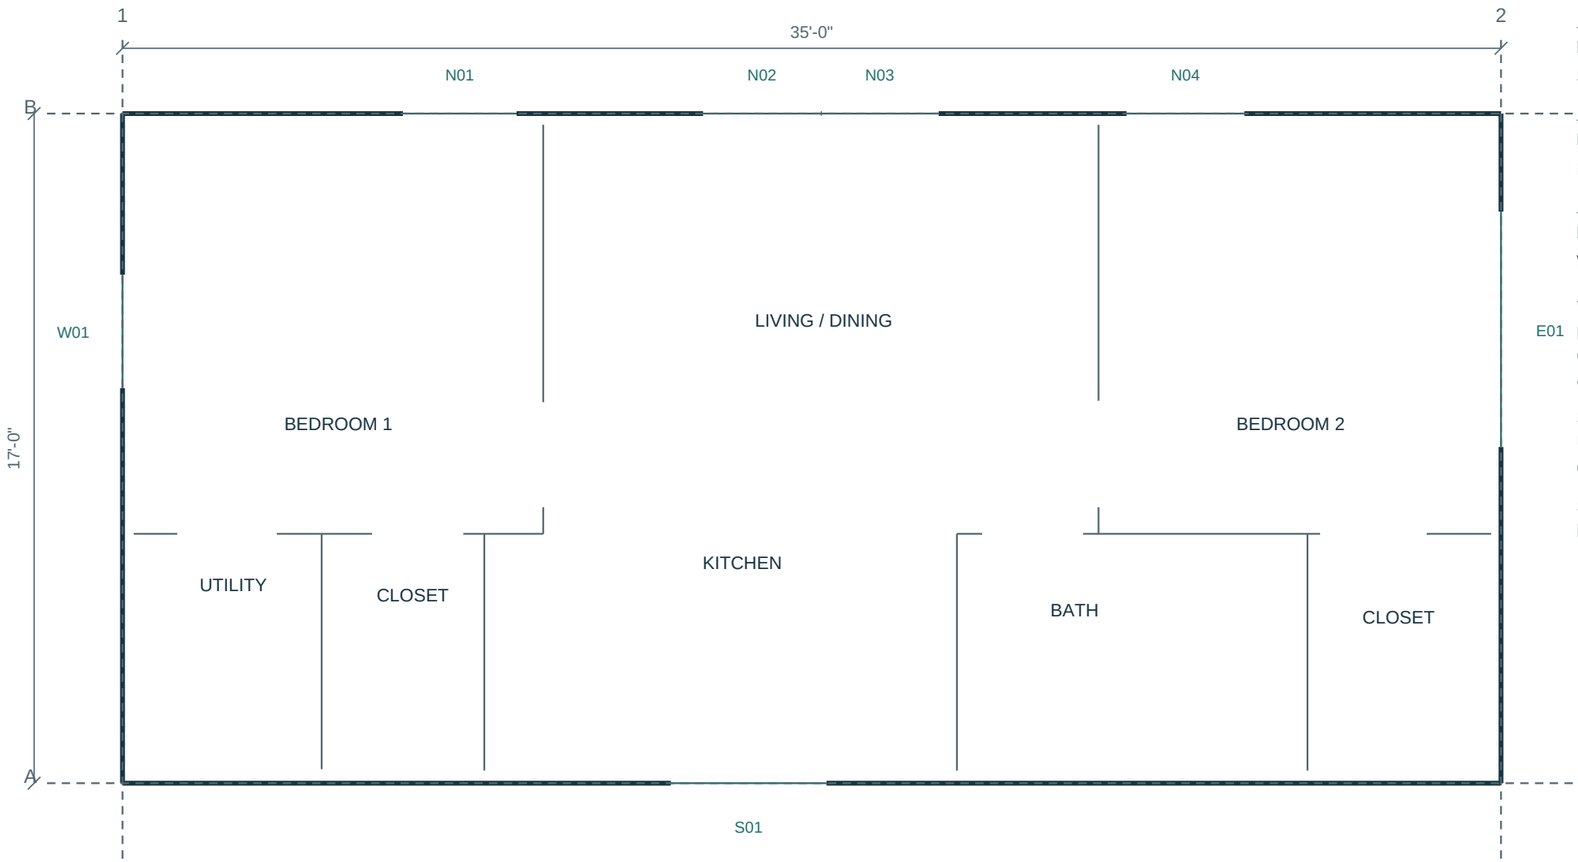

EXTERIOR OPENING SCHEDULE / INCHES

ID	TYPE	START*	END*	PIER*	SOURCE SIZE
T / NORTH | WALL 420 | END PIER* 78.2					
N01	WINDOW	85.5	120.1	85.5	36 x 60
N02	DOOR	176.9	212.8	56.8	36 x 80
N03	VENT	212.8	248.7	0	36 x 80
N04	WINDOW	305.9	341.8	57.3	36 x 60
B / SOUTH | WALL 420 | END PIER* 205.5					
S01	WINDOW	167.1	214.5	167.1	48 x 36
R / EAST | WALL 204 | END PIER* 102.4					
E01	WINDOW	29.9	101.6	29.9	72 x 60
L / WEST | WALL 204 | END PIER* 120.4					
W01	WINDOW	49.1	83.6	49.1	36 x 60

* Approximate trace in inches. Pier is clear plan distance from prior traced edge or starting corner. Nominal sizes are source elevation labels. Confirm frame OD, RO, sill and head with selected assemblies.

Short elevations show 201.5 in versus the 204 in floor plan depth. Use the floor plan datum for traced stations and reconcile before detailing.

Source interior tags: 28 in closets, 30 in utility and bath, 32 in bedrooms.

DATUM AND STATION METHOD

T/B stations run plan left to right. L/R stations run plan top to bottom. 1-2 and A-B identify the exterior footprint datums. Opening stations are approximate trace measurements from an NTS reference.

Haven exterior opening coordination

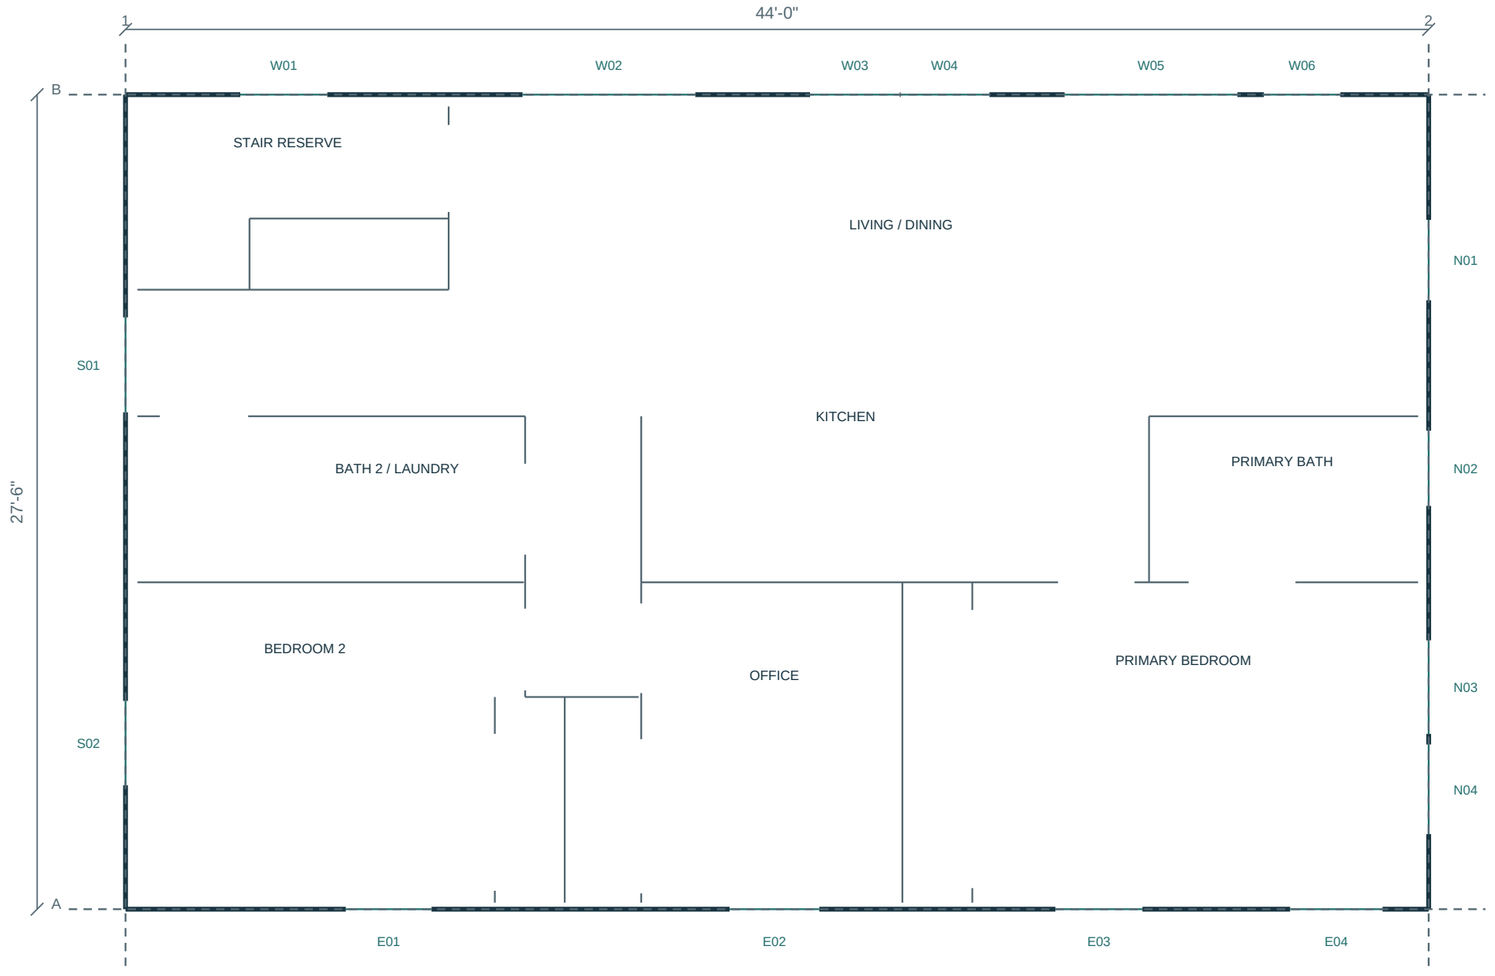

EXTERIOR OPENING SCHEDULE / INCHES

ID	TYPE	START*	END*	PIER*	SOURCE SIZE
T / WEST | WALL 528 | END PIER* 35.8					
W01	WINDOW	46.5	81.8	46.5	VERIFY
W02	WINDOW	160.9	230.9	79.1	71 x 47.5
W03	VENT	277.4	313.7	46.5	37 x 81
W04	DOOR	313.7	350	0	37 x 81
W05	WINDOW	380.5	450.5	30.5	71 x 47.5
W06	WINDOW	461.2	492.2	10.7	30 x 60
B / EAST | WALL 528 | END PIER* 18.7					
E01	WINDOW	89.2	124	89.2	30 x 60
E02	WINDOW	244.8	281.1	120.8	30 x 60
E03	WINDOW	376.8	412	95.7	30 x 60
E04	WINDOW	471.9	509.3	59.9	30 x 60
R / NORTH | WALL 330 | END PIER* 30.4					
N01	WINDOW	50.7	83.3	50.7	VERIFY
N02	WINDOW	136.2	166.6	52.9	30 x 60
N03	VENT	221.1	259	54.5	37 x 81
N04	DOOR	263.3	299.6	4.3	37 x 81
L / SOUTH | WALL 330 | END PIER* 50.2					
S01	DOOR	90.2	128.7	90.2	37 x 82
S02	WINDOW	245.6	279.8	116.9	30 x 60

* Approximate trace in inches. Pier is clear plan distance from prior traced edge or starting corner. Nominal sizes are source elevation labels. Confirm frame OD, RO, sill and head with selected assemblies.

West and north traces disagree with the elevations. W01 and N01 are unconfirmed plan marks. North gable has a separate 12 x 36 callout at ridge; location and RO are TBD. West entry is 36 in in plan versus 37 x 81 in elevation.

Source interior tags: 24, 30, 32 and 36 in. Verify closet pairs, bath slider and stair door.

DATUM AND STATION METHOD

T/B stations run plan left to right. L/R stations run plan top to bottom. 1-2 and A-B identify the exterior footprint datums. Opening stations are approximate trace measurements from an NTS reference.
